


Approve SAR 40M for four regions, Najran, Northern Borders, Al-Baha and Jazan, to close the last gap to 65%

Big idea: The national 65% target is met, but four regions are stuck below it. Put the full SAR 40M into those four, so all four reach it by Dec 2026 instead of as late as 2027.

Najran	Northern Borders	Al-Baha	Jazan
SAR 15M	SAR 9M	SAR 8M	SAR 8M
60.9% today, gap 4.1 pts 21 months to 65% at today's pace	62.7% today, gap 2.3 pts 10 months to 65% at today's pace	62.8% today, gap 2.2 pts 9 months to 65% at today's pace	63.0% today, gap 2.0 pts 7 months to 65% at today's pace

Decision requested today: release SAR 20M now and SAR 20M after a June 2026 checkpoint.

Nationally, Tayseer is on track: 66.2% digital adoption, above 65% since August 2025

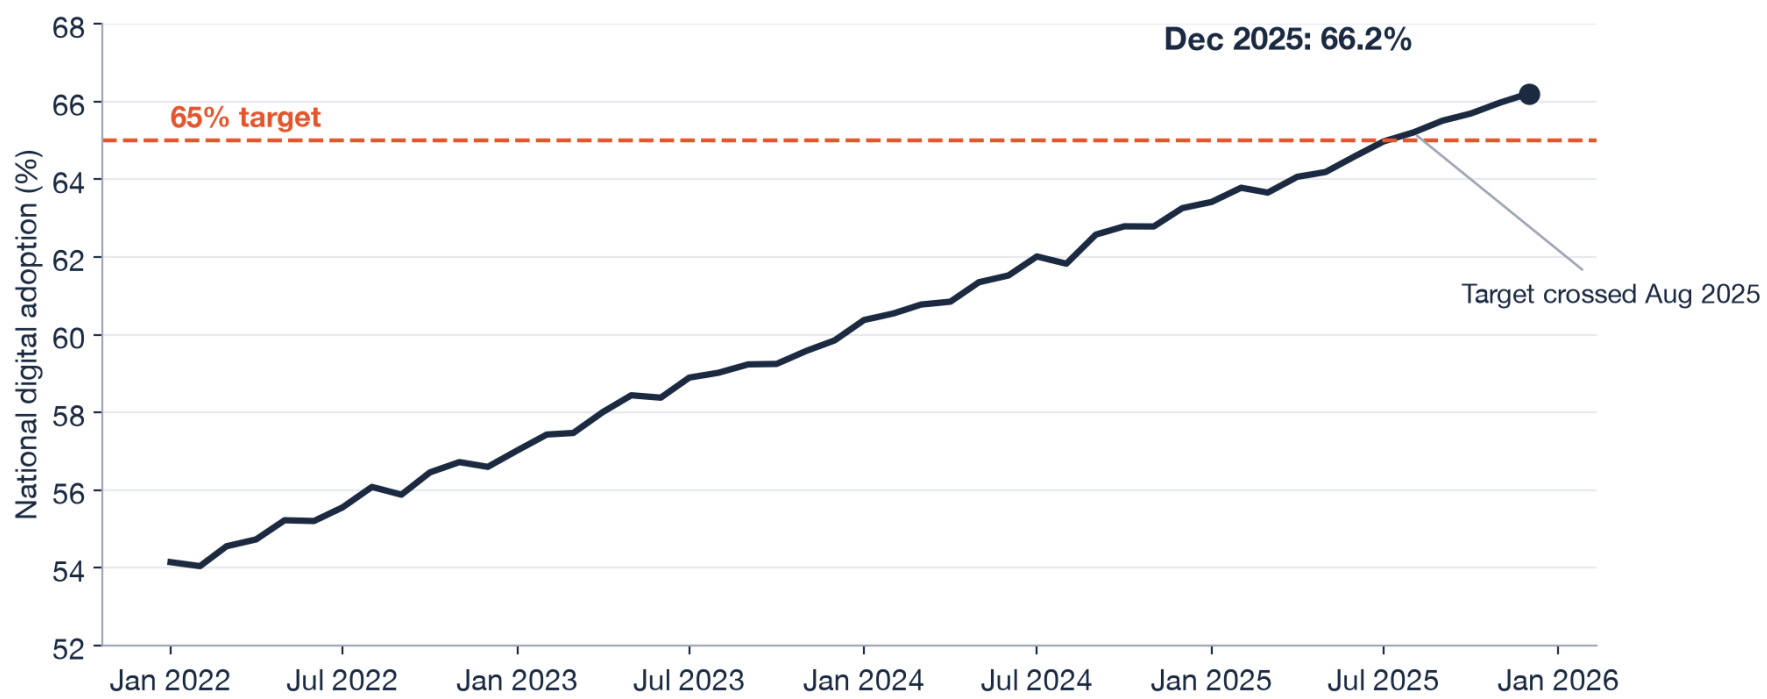

66.2%

National adoption, Dec 2025


+2.9 pts

Change vs Dec 2024

Aug 2025

Month the 65% target was crossed

But 8 of 13 regions are still below 65%, and the national average hides them

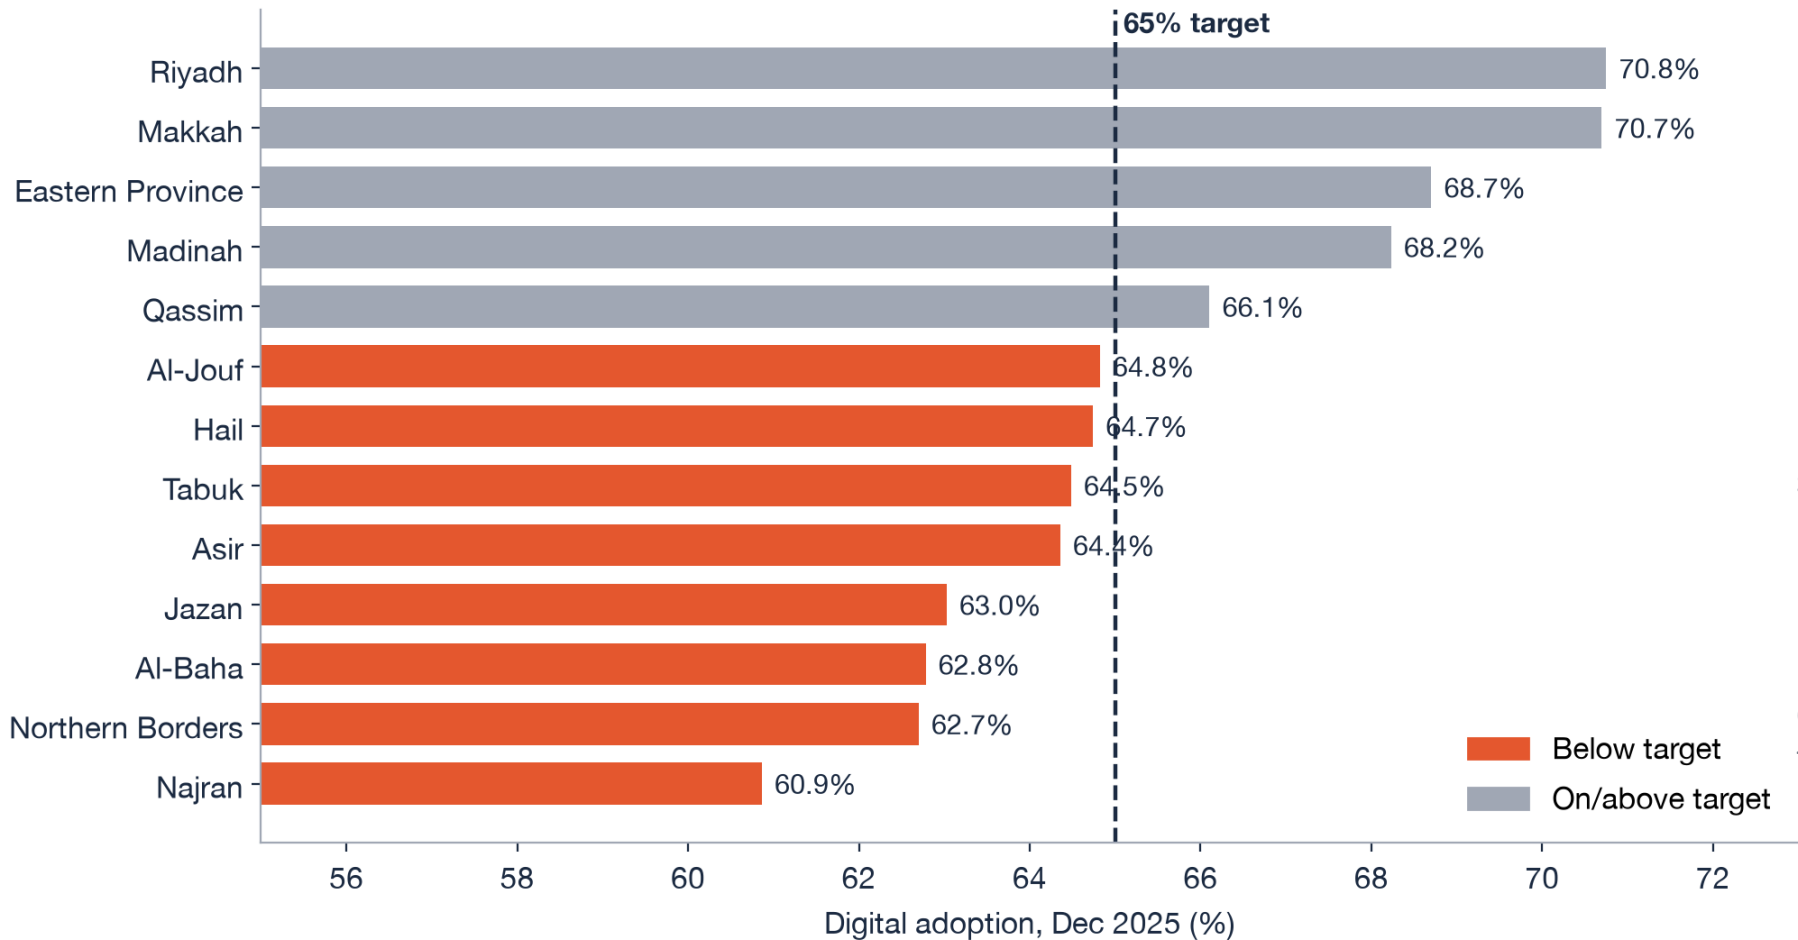

8 regions

below the 65% target in Dec 2025


60.9%

Najran, the lowest region, is 4.1 pts short

5 regions

carry the national average above target

Four regions will close the gap on their own within 3 months; four will not, and Najran needs 21

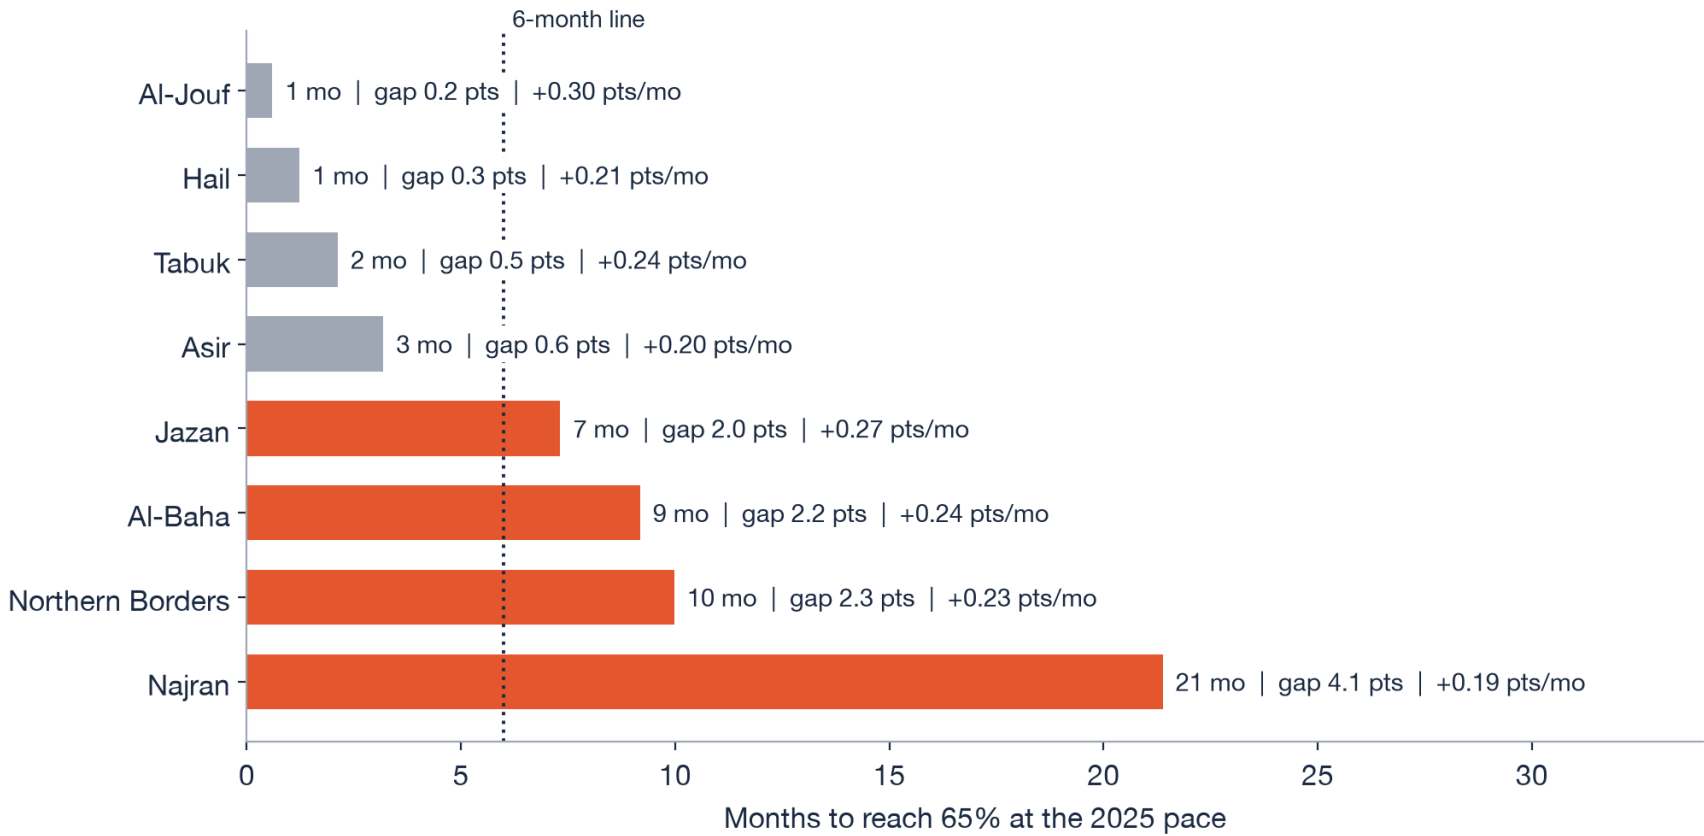

Where the gap sits

56.8%

Complaints digital adoption in the 4 priority regions (national: 62.1%)


All 8

service categories in these regions trail the national rate by 3–5 pts, so the problem is regional, not one product

We compared three ways to spend SAR 40M; only one aims every riyal at a gap that won't close by itself

Criteria	A · Spread evenly	B · Focus on 4 laggards	C · National campaign
What it is	SAR 5M to each of the 8 regions below 65%	SAR 40M split across Najran, N. Borders, Al-Baha, Jazan by gap size	One national push to move branch & call-centre users to app/web
Hits the gap that won't self-close?	Half: SAR 20M goes to regions closing in ≤3 months	Yes: 100% to regions needing 7–21 months	Mostly not: reach is driven by large, on-target regions
Najran funding	SAR 5M	SAR 15M	Unclear / diluted
Main risk	Too thin to change pace anywhere	Concentration: depends on local delivery	Lifts the average again, leaves gaps

Recommend option B: weight the SAR 40M by gap and bring all four regions to 65% by December 2026

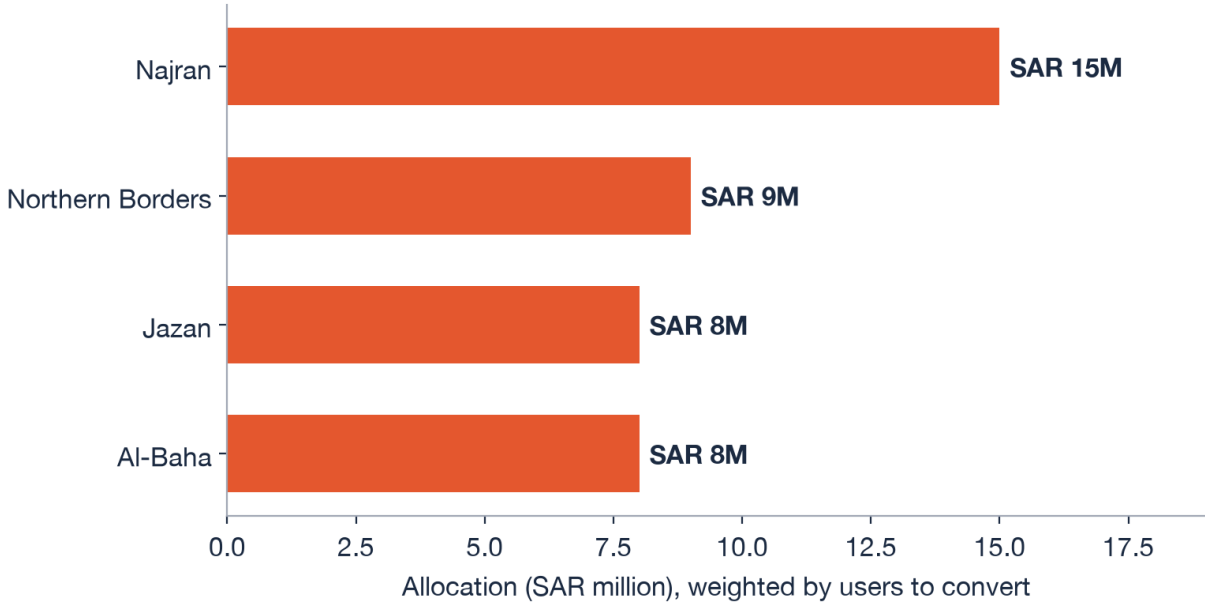

What the money buys

- 1 Digitise Complaints & Permits, the weakest journeys
- 2 Assisted-digital desks in branches (branch adoption 53% vs app 75%)
- 3 Local awareness & onboarding in the four regions

Expected effect

All 4 regions ≥ 65% by Dec 2026 (Najran: ~Sep 2027 at today's pace)
Najran pace must rise +0.19 → +0.34 pts/month
Digital txn ≈ SAR 15 vs SAR 24 assisted; higher CSAT

Approve SAR 40M for the four regions today, released in two tranches with a June 2026 checkpoint

Decision today

Approve SAR 40M

Najran, Northern Borders, Al-Baha and Jazan

Tranche 1 · now

SAR 20M to start the Complaints/Permits fixes and branch desks

Tranche 2 · June 2026

SAR 20M, released region by region if the checkpoint is met

June 2026 checkpoint (halfway to 65%)

Region	Dec 2025	Must reach by Jun 2026
Najran	60.9%	≥ 62.9%
Northern Borders	62.7%	≥ 63.9%
Al-Baha	62.8%	≥ 63.9%
Jazan	63.0%	≥ 64.0%

Tracked monthly on the Tableau dashboard. A missed checkpoint sends that region's tranche 2 to its weakest journey or to the next lagging region.
